BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer, Yelahanka Division.
Project Name	:	"Development and Construction of Auditorium and Toilet at Yelahanka PU Collage in Ward No-01 of Yelahanka Sub Division."
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	19-Dec-20
Project End Date	:	17-Jun-21
Project Length in Months	:	180 Days

SL No	*Assignment*	*Unit*	*Tender Qnty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*
1	Providing and constructing load bearing wall with solid concrete blocks having block density not less than 1800kg/m3 having a minimum average compressive strength of 5.00 N/mm2 confirming to IS 2185 (Part 1):2005 and	Sqm	868.12	226.43	26	30-01-21	24-02-21	25
2	Providing and laying in position reinforced cement concrete of Design Mix M20 with OPC @ 320kgs, with 20mm and down size graded granite metal coarse aggregates @0.69cum and fine aggregtes@ 0.460 cum,	Cum	4.80	3.35	70	30-01-21	04-02-21	5
3	Providing T.M.T steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and I or welding wherever required, tying with binding wire and anchoring to the adjoining	tonne	11.11	5.78	52	26-12-20	25-03-21	89
4	Providing 15mm thick plain plastering in single coat to external masonry surfaces, in cement mortar 1:4 (1 cement : 4 fine sand) including providing & mixing water proofing compound of approved quality and	Sqm	2233.23	146.49	7	04-02-21	01-03-21	25
5	Providing and finishing external walls in two coats with waterproof cement paint of approved brand and shade to give an even shade after throughly brooming the surface to remove all dirt and loose powdered material, free from mortar	Sqm	3828.31	2995.33	78	14-02-21	11-03-21	25
6	Providing barbed Gl wire fencing of 12x12 gauge drawn into stone pillars or iron pillars including drawing in holes wherever necessary excluding the cost of pillars but including the cost of barbed wire and binding wire etc.,	m	18554.34	173.20	1	02-02-21	12-02-21	10
10	Providing and laying in position plain cement concrete of Mix 1:2:4 with OPC @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.878 cum and fine aggregtes @ 0.53cum, machine mixed,	Cum	86.49	17.08	20	25-01-21	05-02-21	11
13	Providing applying two coats of wall putty to inside plastered walls and ceiling using white cement putty. Scrapping and levelling the surface using steel blade and preparing the surface even and smooth by using	Sqm	950.53	2875.31	100	15-03-21	30-03-21	15

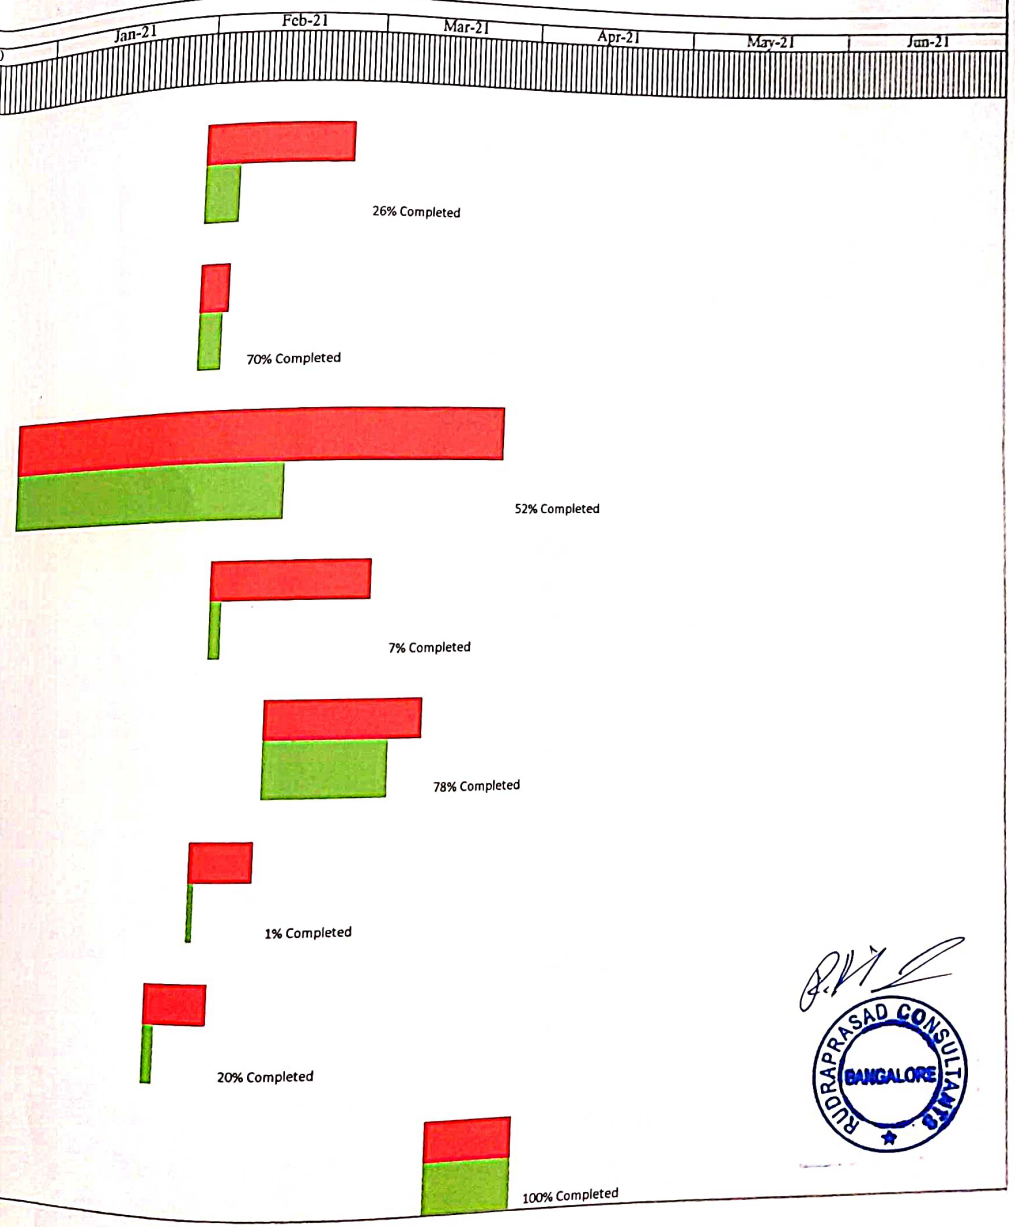

RUDRAPRASAD CONSULTANTS BANGALORE

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer, Yelahanka Division.
Project Name	:	"Development and Construction of Auditorium and Toilet at Yelahanka PU Collage in Ward No-01 of Yelahanka Sub Division."
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	19-Dec-20
Project End Date	:	17-Jun-21
Project Length in Months	:	180 Days

Sl No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
63	Construction of dry lean cement concrete mix CC 1:5:10 with OPC cement @160Kgs. with 25mm and down size graded granite metal coarse aggregate at 0.86cum	Cum	135.00	216.16	100	28-01-21	11-02-21	14
64	Constructing un-reinforced, plain cement concrete for pavements using Grade concrete M30 over a prepared base with OPC coarse aggregate at 0.69 cum, fine aggregates at 0.46 cum,Coarse and fine aggregate	Cum	270.00	288.21	100	08-02-21	22-02-21	14
70	Earthwork excavation by mannal means for roads, drains & similar works in ordinary soil excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications	Cum	64.20	3.85	100	09-02-21	17-02-21	8
71	Plain cement concrete M10 mix with crushed stone aggregate 40mm nominal size mechanically mixed, placed in foundation and compacted by vibration including curing including cost of materials, labour,	Cum	10.78	1.28	100	10-02-21	20-02-21	10
72	Providing and fixing pre cast solid cement concrete kerb stones made out of C.C. 1:2:4 with top and bottom width 114 and 165 mm respectively, 400mm high and 450mm in length finished with CM 1:3 plastering and finishing cutting,	m	488.89	143.00	29	10-02-21	20-02-21	10
73	Painting two coats after filling the surface with synthetic enamel paint in approved shades on new plastered concrete surfaces, with materials, labour complete as per specifications.	Sqm	59.40	25.66	43	15-02-21	25-02-21	10
74	Providing T.M.T. steel reinforcement for R.C.C. work including straightening, cutting, bending, hooking, placing in position, lapping and/or welding wherever required, tying with binding wire and anchoring to the adjoining members	Tonne	1.12	23.66	100	24-01-21	20-02-21	27
77	Earthwork excavation by manual means for foundation of buildings, water supply and sanitary lines and electrical conduits etc, either in pits or in trenches 1.5m and above in width, in soil not exceeding 1.5 m. in depth including dressing the bottom	Cum	71.91	78.76	100	19-12-20	24-12-20	5

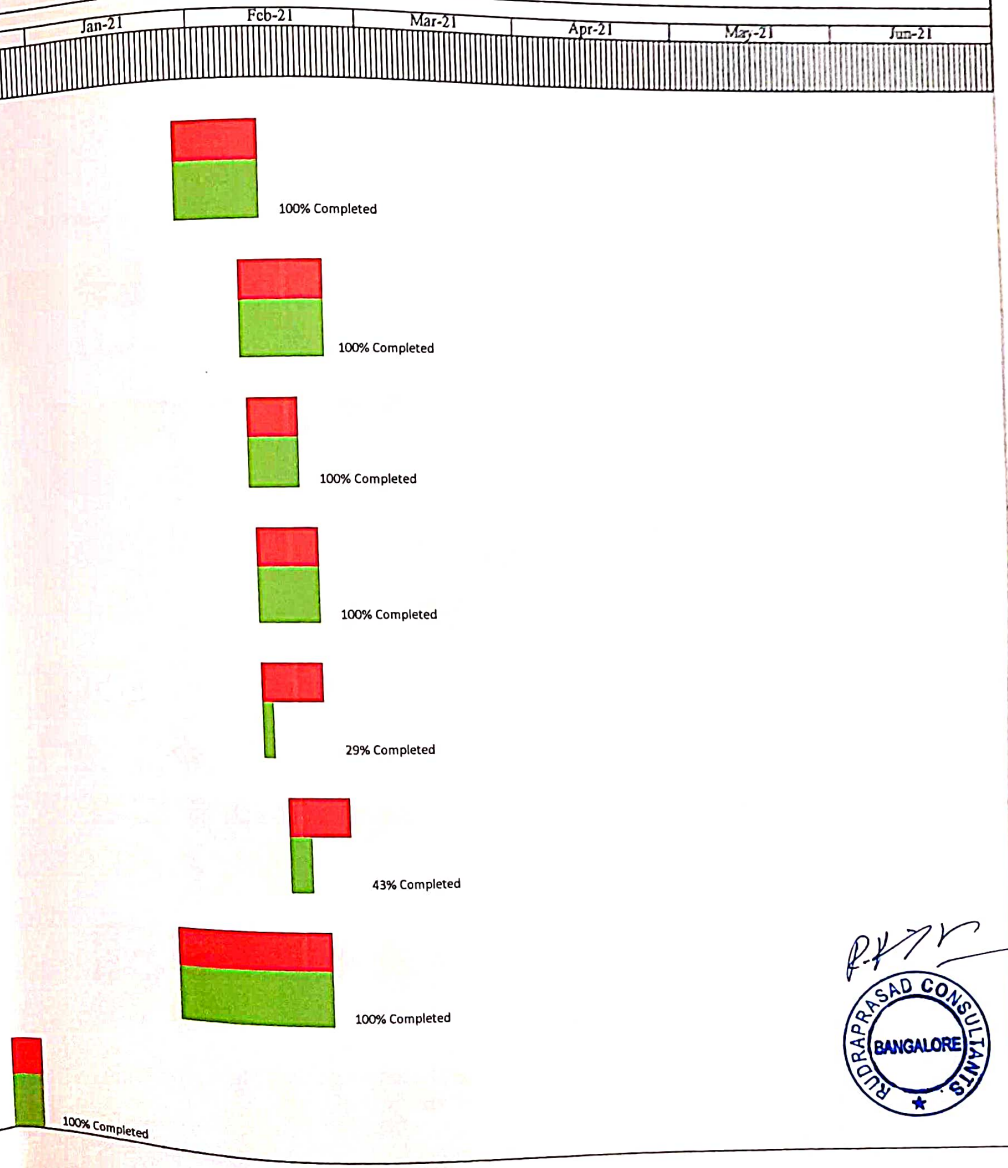

RUDRAPRASAD CONSULTANTS BANGALORE
